
NYCRUNS Prospect Park 5K 2026 #1


Brooklyn, New York


Measured by Matthew Slocum (WA-A) | 28 October 2026 | matt@precisioncoursedesign.com

Except as noted, this course was measured using the full width of the road and the shortest possible route

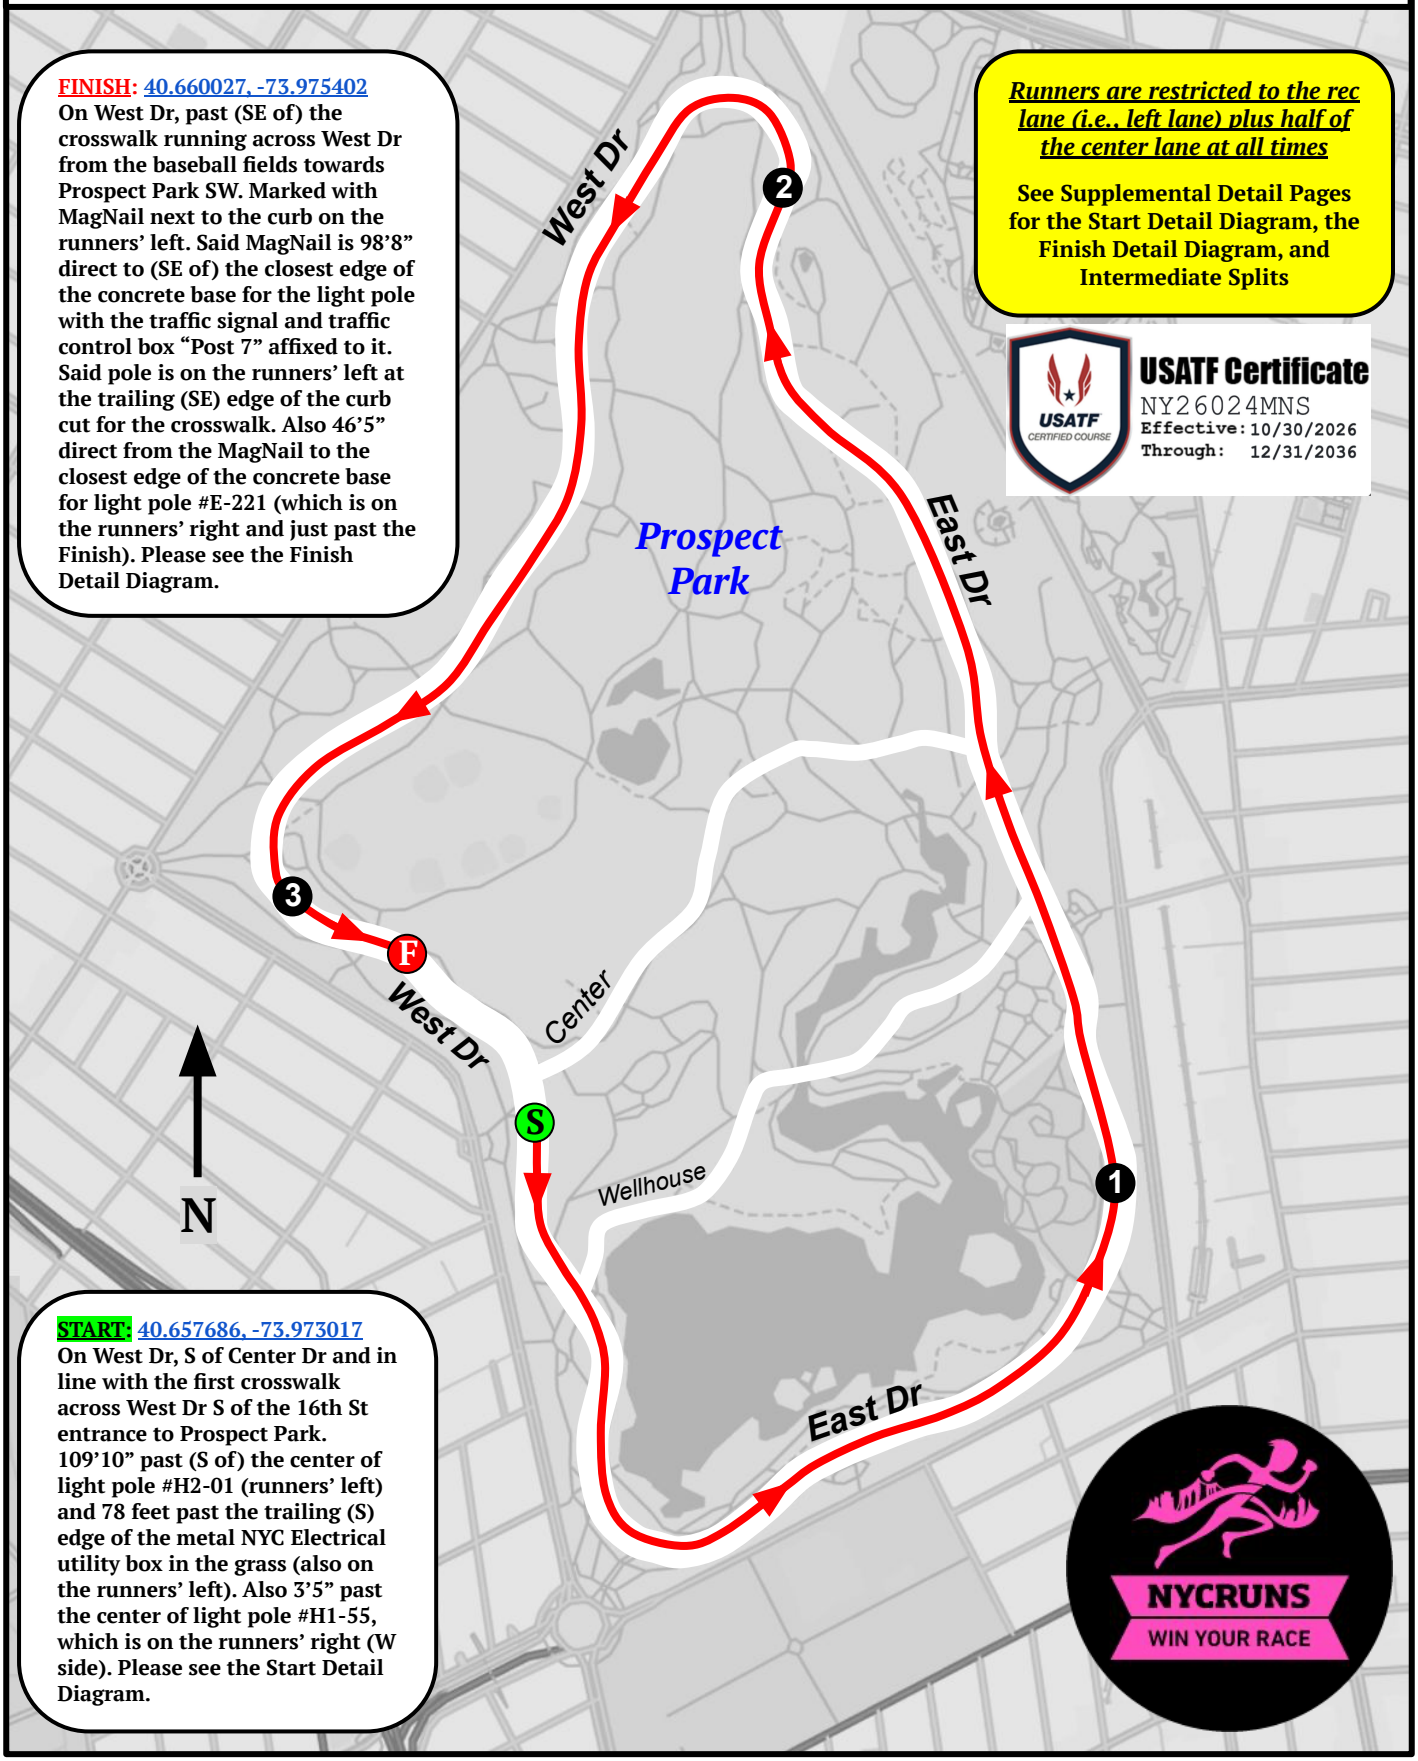

START DETAIL

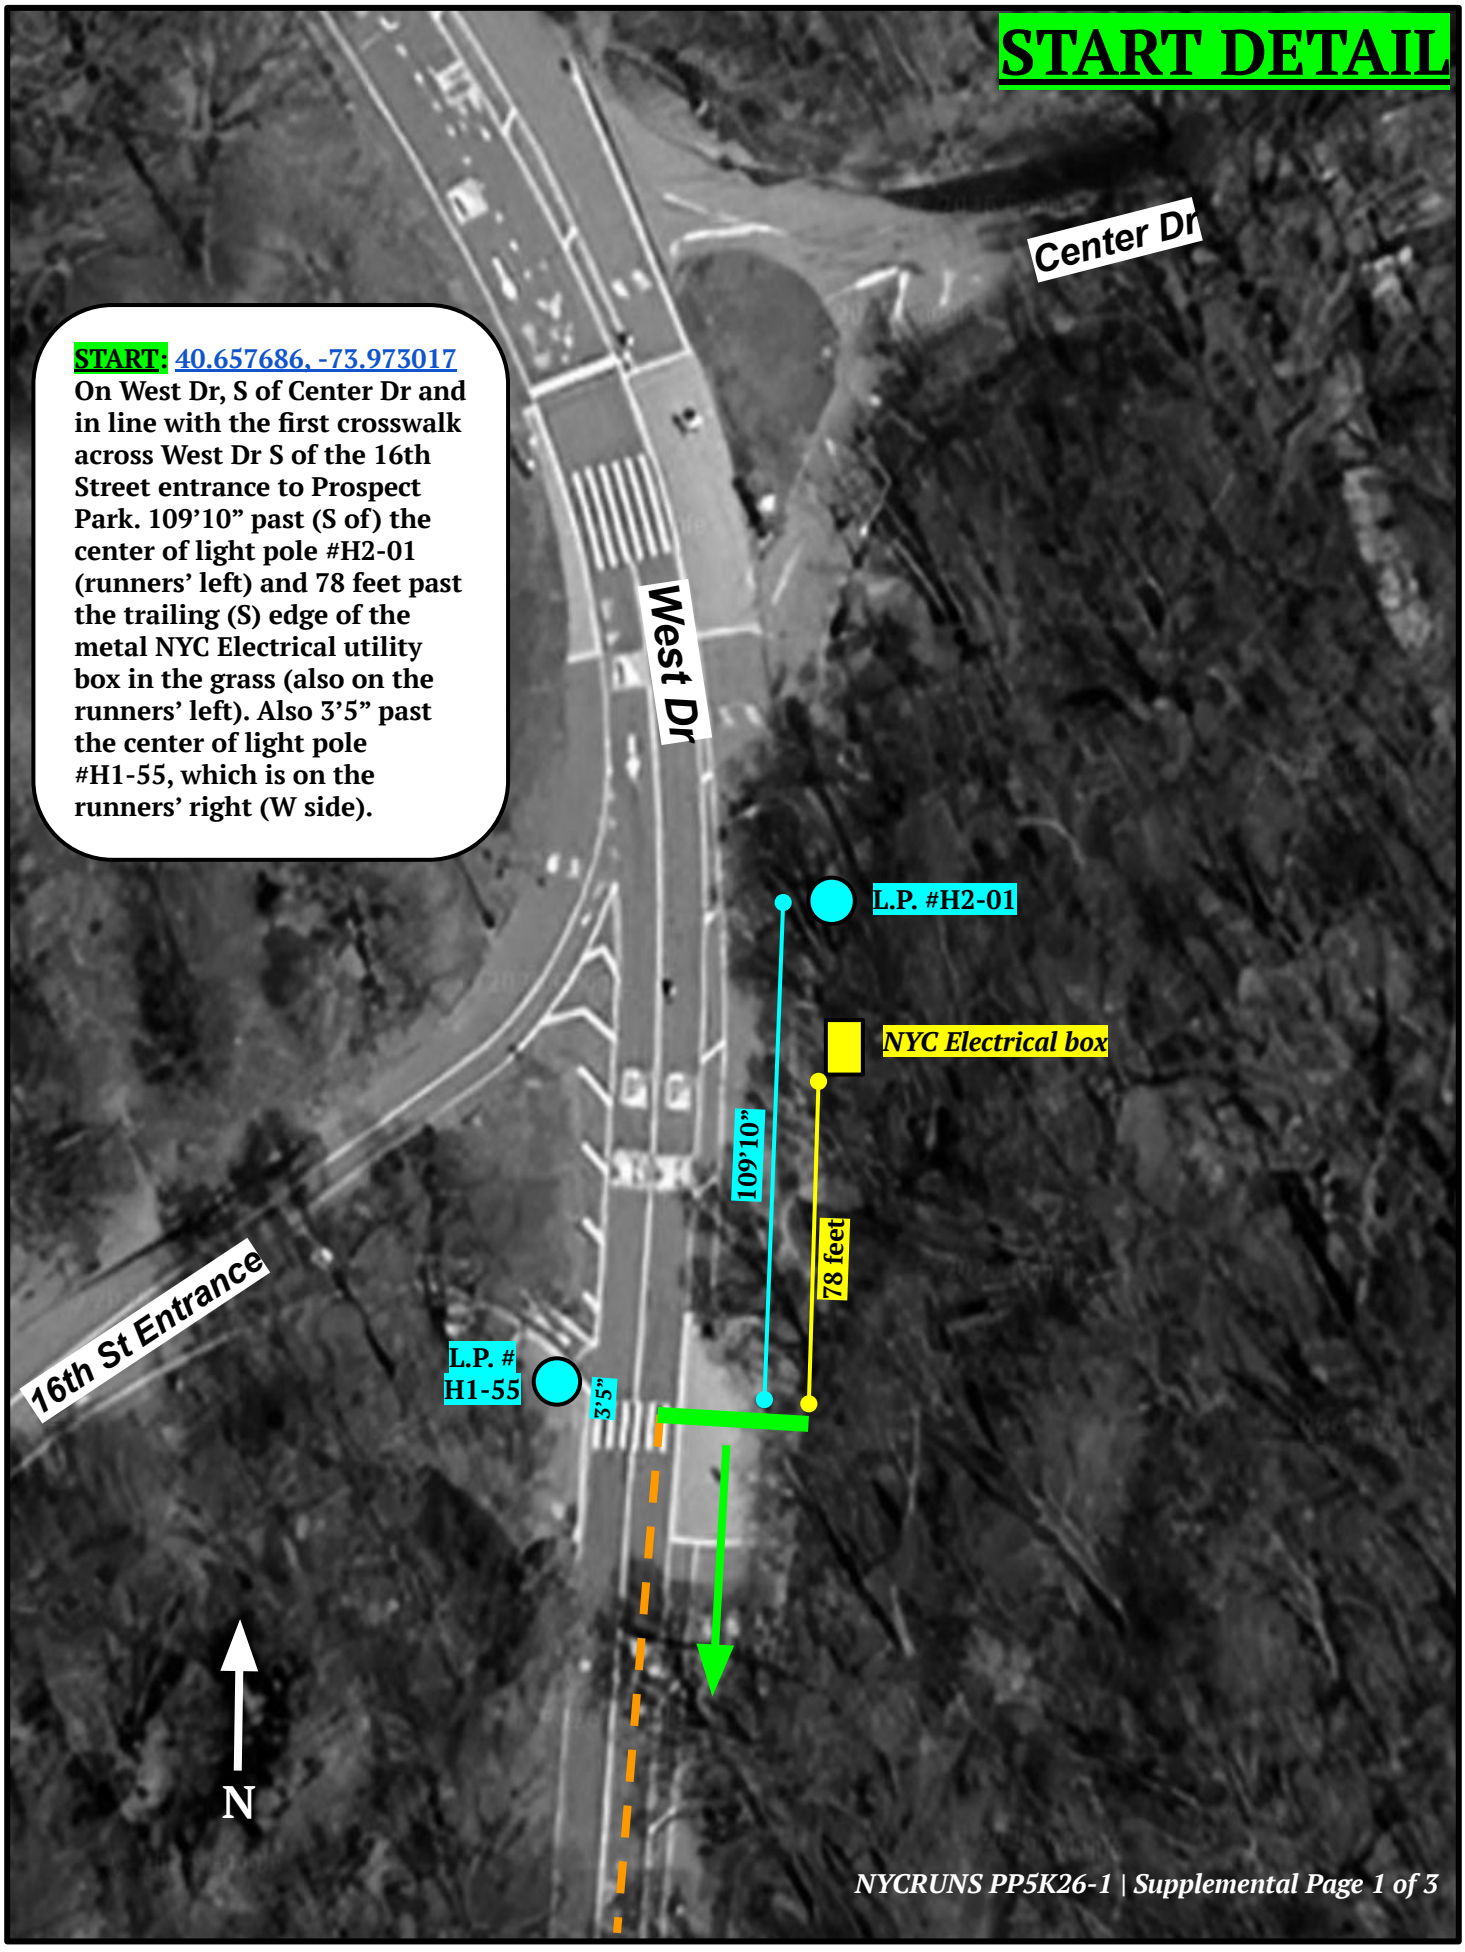

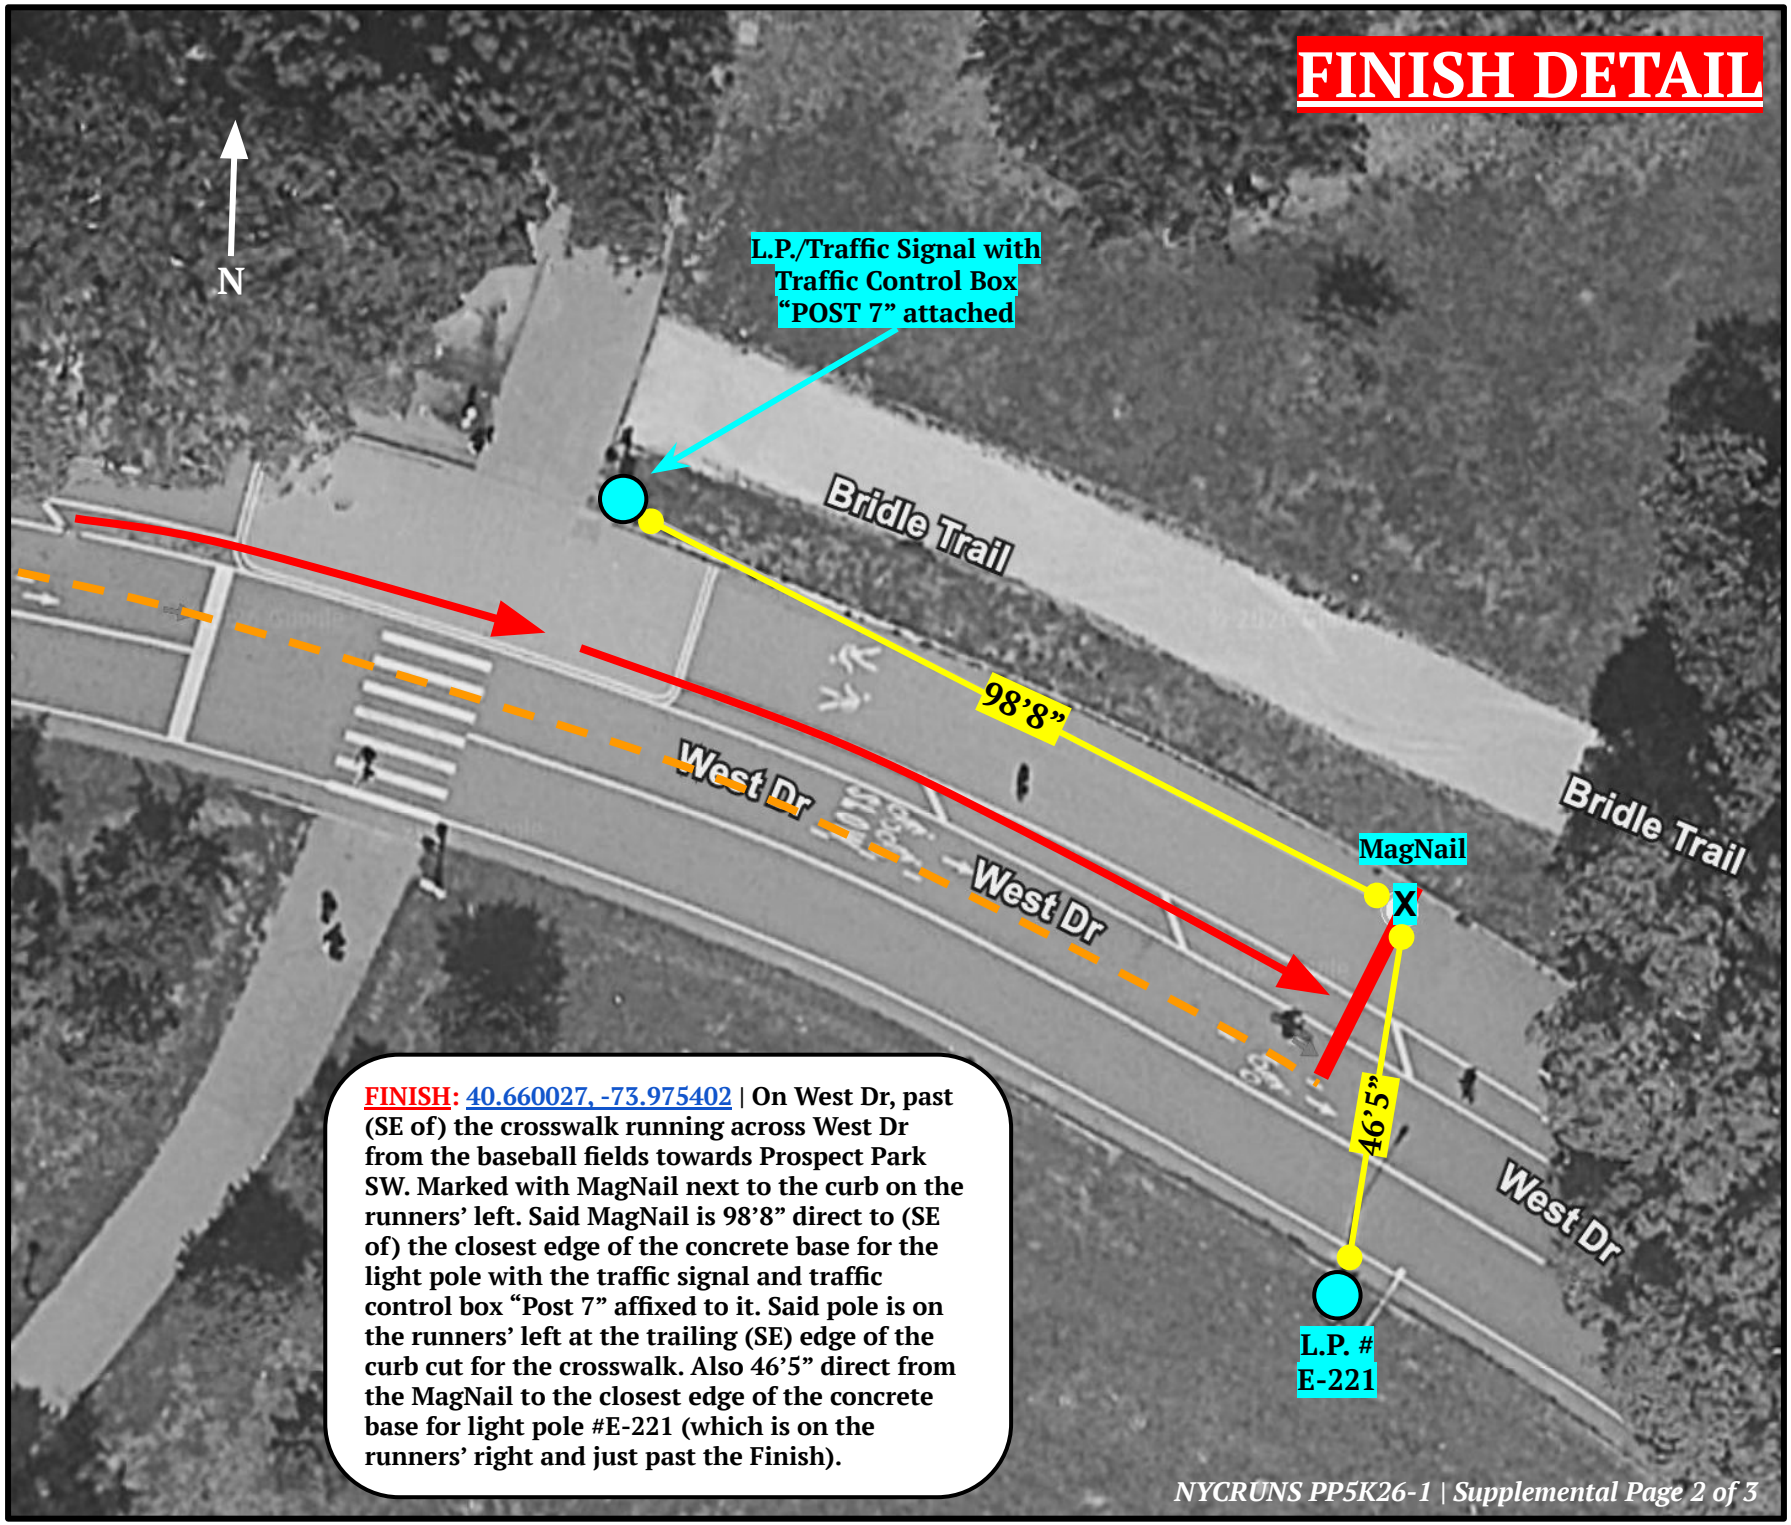
FINISH DETAIL
N
L.P./Traffic Signal with
Traffic Control Box
"POST 7" attached
Bridle Trail
98'8"
West Dr
West Dr
Bridle Trail
MagNail
X
46'5"
West Dr
L.P. #
E-221
FINISH: 40.660027, -73.975402 | On West Dr, past (SE of) the crosswalk running across West Dr from the baseball fields towards Prospect Park SW. Marked with MagNail next to the curb on the runners' left. Said MagNail is 98'8" direct to (SE of) the closest edge of the concrete base for the light pole with the traffic signal and traffic control box "Post 7" affixed to it. Said pole is on the runners' left at the trailing (SE) edge of the curb cut for the crosswalk. Also 46'5" direct from the MagNail to the closest edge of the concrete base for light pole #E-221 (which is on the runners' right and just past the Finish).

NYCRUNS Prospect Park 5K 2026 #1

Course Locations

START: 40.657686, -73.973017 | On West Dr, S of Center Dr and in line with the first crosswalk across West Dr S of the 16th Street entrance to Prospect Park. 109'10" past (S of) the center of light pole #H2-01 (runners' left) and 78 feet past the trailing (S) edge of the metal NYC Electrical utility box in the grass (also on the runners' left). Also 3'5" past the center of light pole #H1-55, which is on the runners' right (W side). Please see the Start Detail Diagram.

Mile 1: 40.656824, -73.962886 | On East Dr, near the SE corner of the park. Past (N of) the Parkside Ave/Ocean Ave entrance, near the skating rink, and before (S of) the LeFrak Center. More specifically, 9'3" before (S of) light pole #L10 (on the runners' right).

2.5 km: 40.664485, -73.965808 | On East Dr, past (N of) Center Dr and between the Carousel and the California Sea Lion Pool. 91 feet past light pole #106 (on the runners' left) and 27 feet before (S of) the unmarked light pole on the runners' right.

Mile 2: 40.670042, -73.968667 | On East Dr, near the top of the hill. 113 feet before (S of) the silver light pole on the runners' left with Call Box #PPP6813 affixed to it.

Mile 3: 40.660658, -73.977282 | On West Dr, past (SE of) the park entrance from Bartel-Pritchard Square (Prospect Park W & Prospect Park SW). 88 feet before (NW of) light pole #118 (on the runners' right). Said light pole has multiple signs affixed to it, the top of which reads "All Times Keep Left/Right". Also 40 feet past (SE of) the unmarked light pole on the runners' left, which has a directional sign for "LeFrak Center at Lakeside" affixed to it.

FINISH: 40.660027, -73.975402 | On West Dr, past (SE of) the crosswalk running across West Dr from the baseball fields towards Prospect Park SW. Marked with MagNail next to the curb on the runners' left. Said MagNail is 98'8" direct to (SE of) the closest edge of the concrete base for the light pole with the traffic signal and traffic control box "Post 7" affixed to it. Said pole is on the runners' left at the trailing (SE) edge of the curb cut for the crosswalk. Also 46'5" direct from the MagNail to the closest edge of the concrete base for light pole #E-221 (which is on the runners' right and just past the Finish). Please see the Finish Detail Diagram.
